Activity ID	Activity description	Dur Days	Early Start	Early Finish	% Comp
MAIN CONSTRUCTION WORKS					
DEMOLITION (BY OTHERS)					
100110	Decant Complete	0	07-DEC-12*		100
100120	Site Establish	24	07-DEC-12	04-FEB-13	100
100130	Retention to Existing Facade	30	15-DEC-12	20-FEB-13	100
100140	Soft Strip	30	15-DEC-12	20-FEB-13	100
100150	Demolition	60	06-FEB-13	02-MAY-13	100
100160	Handover Site to Main Contractor	0	03-MAY-13		100
SITE ESTABLISHMENT					
1030	Site Establish - Site Office & Accommodation	12	03-MAY-13	17-MAY-13	100
300149960	BMC Site Possession	0	03-MAY-13		100
300150210	Site Establishment	12	03-MAY-13	17-MAY-13	100
300151680	Establish Hardstand for Piling Rig	6	03-MAY-13	10-MAY-13	100
300151690	Mobilise Piling Rigs	2	09-MAY-13	10-MAY-13	100
EXCAVATION / RETENTION / FOUNDATION S					
PILING					
110010	Retention Piles - East	12	11-MAY-13	24-MAY-13	100
110020	Retention Piles - South	12	20-MAY-13	03-JUN-13	100
110030	Retention & Building Piles - West	12	25-MAY-13	12-JUN-13	100
110040	Retention Piles - North	14	04-JUN-13	22-JUN-13	100
RETENTION & EXCAVATION					
EAST					
110110	Construct Capping Beam	8	25-MAY-13	04-JUN-13	100
110120	Excavate to 1st Anchor Level	4	15-JUN-13	19-JUN-13	100
110130	Install 1st Row Anchors	7	20-JUN-13	28-JUN-13	50
110140	Spray Walls	8	29-JUN-13	09-JUL-13	50
110150	Excavate to 2nd Anchor Level	2	10-JUL-13	11-JUL-13	0
110160	Install 2nd Row Anchors	6	12-JUL-13	18-JUL-13	0
110170	Spray Walls	8	19-JUL-13	29-JUL-13	0
110180	Final Excavate & Spray	6	30-JUL-13	06-AUG-13	0
SOUTH					
110210	Construct Capping Beam	8	04-JUN-13	15-JUN-13	100
300155970	Excavate to 1st Anchor Level	2	17-JUN-13	18-JUN-13	50
300155980	Install 1st Row Anchors	6	29-JUN-13	05-JUL-13	10
300155990	Spray Walls	8	06-JUL-13	16-JUL-13	15
300156000	Excavate to 2nd Anchor Level	2	17-JUL-13	18-JUL-13	0
300156010	Install 2nd Row Anchors	5	19-JUL-13	25-JUL-13	0
300156020	Spray Walls	6	26-JUL-13	01-AUG-13	0
300156030	Final Excavate & Spray	6	02-AUG-13	09-AUG-13	0
WEST					
110310	Construct Capping Beam	8	13-JUN-13	21-JUN-13	70
300156040	Excavate to 1st Anchor Level	2	22-JUN-13	25-JUN-13	10
300156050	Install 1st Row Anchors	7	06-JUL-13	15-JUL-13	0
300156060	Spray Walls	8	16-JUL-13	25-JUL-13	0
300160530	Excavate & Spray	9	26-JUL-13	06-AUG-13	0
300156070	Final Excavate & Spray	6	07-AUG-13	13-AUG-13	0
NORTH					
110410	Construct Capping Beam	8	25-JUN-13	03-JUL-13	100
300156080	Excavate to 1st Anchor Level	2	04-JUL-13	05-JUL-13	80
300156090	Install 1st Row Anchors	6	16-JUL-13	23-JUL-13	40
300156100	Spray Walls	10	24-JUL-13	03-AUG-13	20
300156110	Excavate to 2nd Anchor Level	3	06-AUG-13	08-AUG-13	0
300156120	Install 2nd Row Anchors	4	09-AUG-13	13-AUG-13	0
300156130	Spray Walls	7	14-AUG-13	22-AUG-13	0
300156140	Final Excavate & Spray	6	23-AUG-13	29-AUG-13	0
FOUNDATION BASEMENT SLABS					
AREA 1 SLAB (LOWER)					
300160550	Pad & Strip Footings	12	10-AUG-13	24-AUG-13	0
300160610	Sub Floor Services	6	22-AUG-13	28-AUG-13	0
300160910	Area 1 Slab (Lower)	6	22-AUG-13	28-AUG-13	0
300160760	Construct Slab on Ground	9	29-AUG-13	07-SEP-13	0
300162710	Erect & Prop Precast	4	10-SEP-13	13-SEP-13	0
AREA 2 SLAB (LOWER)					
300161210	Pad & Strip Footings	12	15-AUG-13	29-AUG-13	0
300161360	Sub Floor Services	6	26-AUG-13	31-AUG-13	0
300161510	Construct Slab on Ground	9	02-SEP-13	12-SEP-13	0
300162120	Erect & Prop Precast	4	13-SEP-13	17-SEP-13	0
AREA 3 SLAB (UPPER)					
300162740	Pad & Strip Footings	9	13-SEP-13	23-SEP-13	0
300162780	Backfill Against Pour 1 Walls	3	14-SEP-13	17-SEP-13	0
300162750	Sub Floor Services	6	24-SEP-13	02-OCT-13	0
300162760	Construct Slab on Ground	9	03-OCT-13	12-OCT-13	0
AREA 4 SLAB (UPPER)					
300162420	Pad & Strip Footings	9	13-SEP-13	23-SEP-13	0
300163580	Backfill Against Pour 1 Walls	3	14-SEP-13	17-SEP-13	0
300162670	Sub Floor Services	6	24-SEP-13	02-OCT-13	0

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity description	Dur Days	Early Start	Early Finish	% Comp
300162700	Construct Slab on Ground	9	03-OCT-13	12-OCT-13	0
AREA 5 SLAB (UPPER)					
300162810	Backfill Against Pour 2 Walls	3	18-SEP-13	20-SEP-13	0
300162830	Pad & Strip Footings	9	18-SEP-13	27-SEP-13	0
300162840	Sub Floor Services	6	01-OCT-13	07-OCT-13	0
300162850	Construct Slab on Ground	9	08-OCT-13	18-OCT-13	0
AREA 6 SLAB (UPPER)					
300162890	Backfill Against Pour 2 Walls	3	21-SEP-13	24-SEP-13	0
300162920	Pad & Strip Footings	9	21-SEP-13	03-OCT-13	0
300162930	Sub Floor Services	6	04-OCT-13	10-OCT-13	0
300162940	Construct Slab on Ground	9	11-OCT-13	22-OCT-13	0
MAIN CONCRETE STRUCTURE					
GROUND LEVEL SLAB					
300152670	FRP 1	16	19-OCT-13	11-NOV-13	0
300152680	FRP 2	16	28-OCT-13	20-NOV-13	0
300152690	FRP 3	16	31-OCT-13	23-NOV-13	0
300152700	FRP 4	16	08-NOV-13	27-NOV-13	0
300152730	FRP 5	16	16-NOV-13	05-DEC-13	0
300150140	FRP 6	16	23-NOV-13	12-DEC-13	0
300152030	Wishbone Beams	30	18-JAN-14	01-MAR-14	0
300152040	FRP 6	12	03-MAR-14	19-MAR-14	0
LEVEL 1 SLAB					
300152710	FRP 1	12	28-NOV-13	12-DEC-13	0
300163550	FRP 2	12	06-DEC-13	20-DEC-13	0
300151860	FRP 3	10	13-DEC-13	16-JAN-14	0
300163560	FRP 4	10	18-DEC-13	24-JAN-14	0
300152720	FRP 5	10	14-JAN-14	01-FEB-14	0
LEVEL 2 SLAB					
300152740	FRP 1	10	13-DEC-13	16-JAN-14	0
300160100	FRP 2	10	21-DEC-13	31-JAN-14	0
300163570	FRP 3	10	18-JAN-14	04-FEB-14	0
300152750	FRP 4	10	30-JAN-14	11-FEB-14	0
LEVEL 3 SLAB					
300152760	FRP 1	11	01-FEB-14	14-FEB-14	0
300152770	FRP 2	11	13-FEB-14	26-FEB-14	0
300152780	FRP 3	11	25-FEB-14	12-MAR-14	0
LEVEL 4 SLAB					
300150190	Level 4 Slab	28	15-FEB-14	24-MAR-14	0
300152790	FRP 1	10	15-FEB-14	27-FEB-14	0
300152800	FRP 2	10	27-FEB-14	13-MAR-14	0
300152810	FRP 3	10	13-MAR-14	24-MAR-14	0
LEVEL 5 SLAB (ROOF)					
300150200	Level 5 Slab (Roof)	28	28-FEB-14	04-APR-14	0
300152820	FRP 1	10	28-FEB-14	14-MAR-14	0
300152830	FRP 2	10	25-MAR-14	04-APR-14	0
300150240	Strip Screens / Formwork	24	29-MAR-14	05-MAY-14	0
300152500	Core Walls Above Level 5, Strip & Handover Lift	15	05-APR-14	01-MAY-14	0
CANTILEVER STRUCTURE					
300152350	Temporary Supports to Level 2 (including footing	4	01-MAY-14	05-MAY-14	0
300152360	Steel, Deck & Bracing Levels 2 - 5	8	06-MAY-14	15-MAY-14	0
300152410	Final Connections & Remove Temporary Supports	2	16-MAY-14	17-MAY-14	0
300152400	Reo & Pour Levels 2 - 5	7	19-MAY-14	27-MAY-14	0
ROOF WORKS					
LEVEL 5 ROOF STRUCTURE					
300152050	Steel, Deck, Reo, Pour	12	05-APR-14	28-APR-14	0
UPPER ROOF STRUCTURE					
300152420	Structural Steel	12	29-APR-14	13-MAY-14	0
300152430	Claddding to Upper Roof	12	14-MAY-14	28-MAY-14	0
ROOF OVER ATRIUM					
300152060	LVL Clad Steel Truss Over Atruim (2 No.)	2	21-MAY-14	22-MAY-14	0
300152070	LVL Box Beams Over Atrium (5 No.)	5	23-MAY-14	29-MAY-14	0
300152080	LVL Coffers	9	30-MAY-14	12-JUN-14	0
300152090	Steel Framing Support for Glazed Roof / Gutters	10	13-JUN-14	25-JUN-14	0
300157510	Roof Glazing Modules	10	26-JUN-14	08-JUL-14	0
ATRIUM WORKS & SPECIALISED STRUCTURES					
JUNGLE JIM STRUCTURE					
300152160	Level 1 - Erect Steel / Deck / Reo (Incl Tempora	8	13-DEC-13	21-DEC-13	0
300152170	Level 2 - Erect Steel / Deck / Reo - Pour with L	6	18-JAN-14	30-JAN-14	0

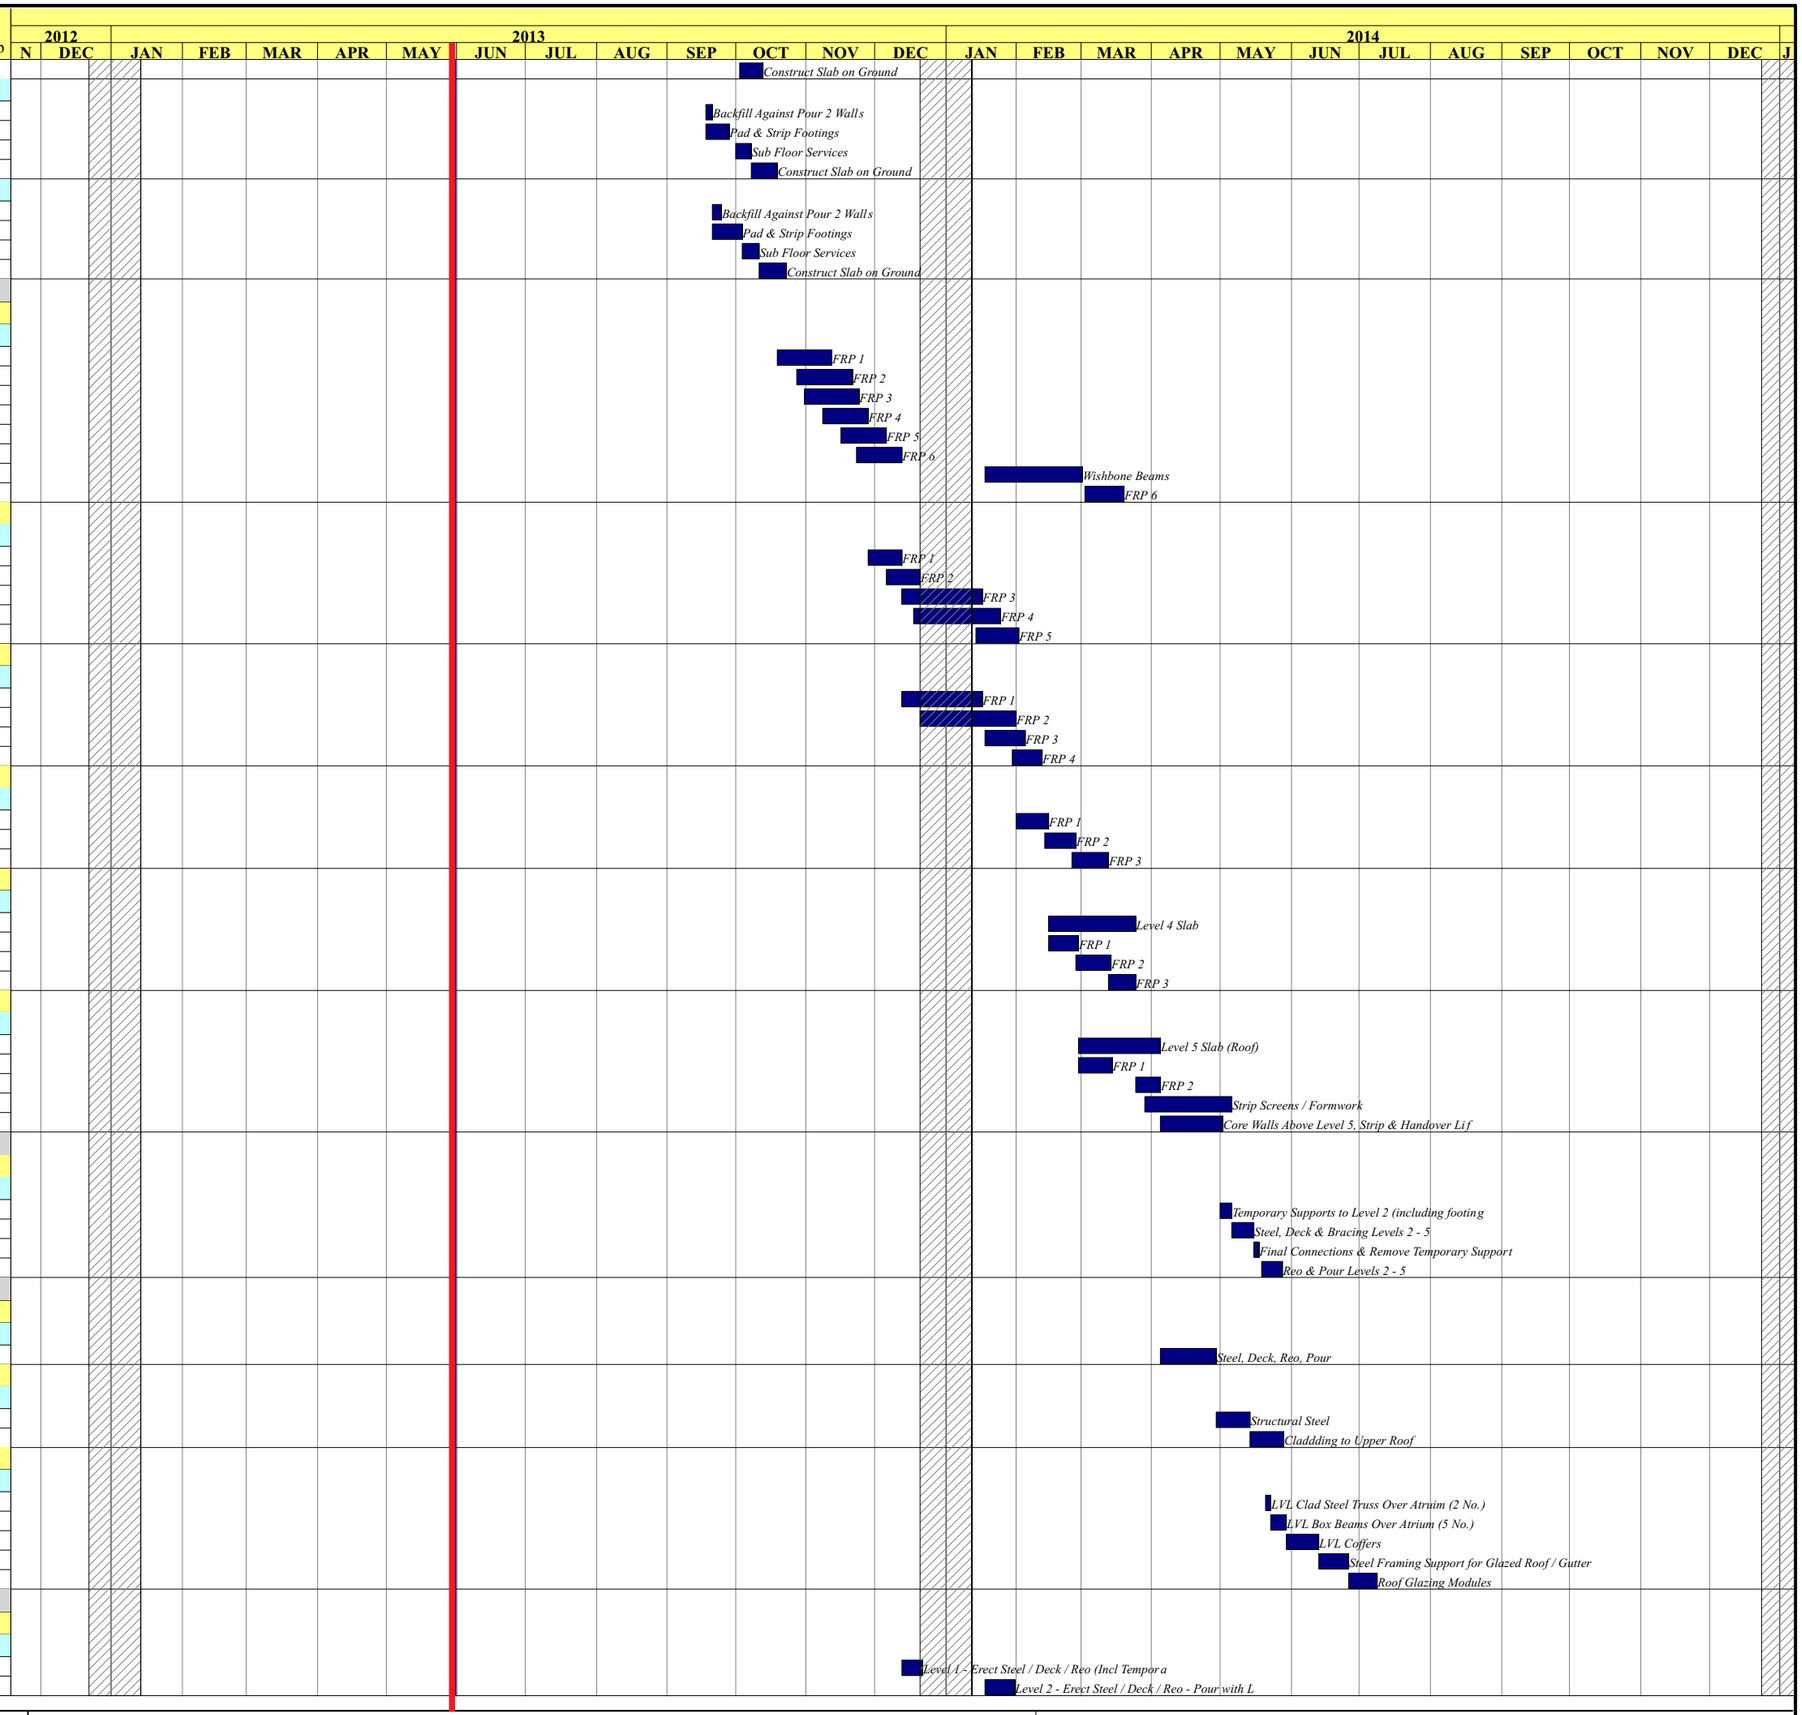

© Primavera Systems, Inc.

Date	Revision	Checked	Approved

Activity ID	Activity description	Dur Days	Early Start	Early Finish	% Comp
300152180	Level 3 - Erect Steel / Deck / Reo - Pour with L	6	25-FEB-14	03-MAR-14	0
300152190	Level 4 - Erect Steel / Deck / Reo / Pour	8	25-MAR-14	02-APR-14	0
300152220	Connect & Tension Macalloy Hangers / Remove Temp	3	03-APR-14	05-APR-14	0
300152660	Level 5 - Erect Steel / Deck / Reo / Pour	6	03-APR-14	09-APR-14	0
LINK BRIDGE					
300152200	Level 2 - East - Erect Steel / Deck / Reo (Incl	6	03-FEB-14	08-FEB-14	0
300152210	Connect & Tension Hangers / Remove Temporay Work	3	25-MAR-14	27-MAR-14	0
ATRIUM STEEL STAIR					
300152230	Steel Framing	4	06-MAY-14	09-MAY-14	0
HANGING STUDIO STEEL FRAME					
300150570	Level 2 - Studio - Erect Steel & Plate (Incl Tem	4	06-MAY-14	09-MAY-14	0
300150580	Level 3 - Project Space - Erect Steel & Plate	2	10-MAY-14	13-MAY-14	0
300150560	Level 4 - RHDS - Erect Steel & Plate	2	14-MAY-14	15-MAY-14	0
300151070	Tension Connection / Remove Temporary Supports	6	23-MAY-14	30-MAY-14	0
Y-STAIR STRUCTURE					
+		12	06-MAY-14	20-MAY-14	0
INTERNAL CLADDING					
+ *HERITAGE FACADE*					
		68	07-APR-14	11-JUL-14	0
+ *HANGING STUDIO*					
		48	09-JUL-14	05-SEP-14	0
FINISHES TO ATRIUM					
+ *MESH BALUSTRADE*					
		60	09-JUL-14	20-SEP-14	0
LIFT & PLANT					
300150270	Load Roof Plant	6	29-APR-14	05-MAY-14	0
300150290	Installation to Lift Motor Room	48	02-MAY-14	03-JUL-14	0
300150830	Install Plant	36	06-MAY-14	21-JUN-14	0
300150300	Lifts Available for Builders Use	0		04-JUL-14	0
300158720	Plant Commissioning	42	17-OCT-14	11-DEC-14	0
FACADE					
+ GROUND FLOOR					
		60	20-MAR-14	12-JUN-14	0
+ LEVEL 1					
		60	05-APR-14	30-JUN-14	0
+ LEVEL 2					
		58	01-MAY-14	15-JUL-14	0
+ LEVEL 3					
		58	14-MAY-14	28-JUL-14	0
+ LEVEL 4					
		58	27-MAY-14	09-AUG-14	0
+ HOIST LOCATION					
		48	29-AUG-14	28-OCT-14	0
JOSEPH REID FACADE WORKS					
+		132	15-MAR-14	05-SEP-14	0
SERVICES & FINISHES					
BASEMENT					
+ *SERVICES ROUGH IN & CORE WALLS*					
		69	12-FEB-14	17-MAY-14	0
+ *PLANTROOM - COMMS ROOM*					
		42	14-APR-14	16-JUN-14	0
+ *PLANTROOM - NORTHERN*					
		138	14-APR-14	16-OCT-14	0
+ *PLANTROOM - PUMP ROOM*					
		54	14-APR-14	01-JUL-14	0
+ *PLANTROOM - SWITCHROOM*					
		78	14-APR-14	31-JUL-14	0
+ *PLANTROOM - SOUTHERN PLANTROOM*					
		90	14-APR-14	15-AUG-14	0
+ *LARGE LECTURE*					
		146	14-APR-14	25-OCT-14	0
+ *MEDIUM LECTURE 1*					
		120	02-MAY-14	03-OCT-14	0
+ *MEDIUM LECTURE 2*					
		120	17-MAY-14	18-OCT-14	0
+ *LIBRARY - STAFF WORK SPACE*					
		86	10-APR-14	07-AUG-14	0
+ *LIBRARY - MEETING & PROJECT ROOMS*					
		86	03-MAY-14	22-AUG-14	0
+ *LIBRARY - COLLECTION*					
		98	10-APR-14	22-AUG-14	0

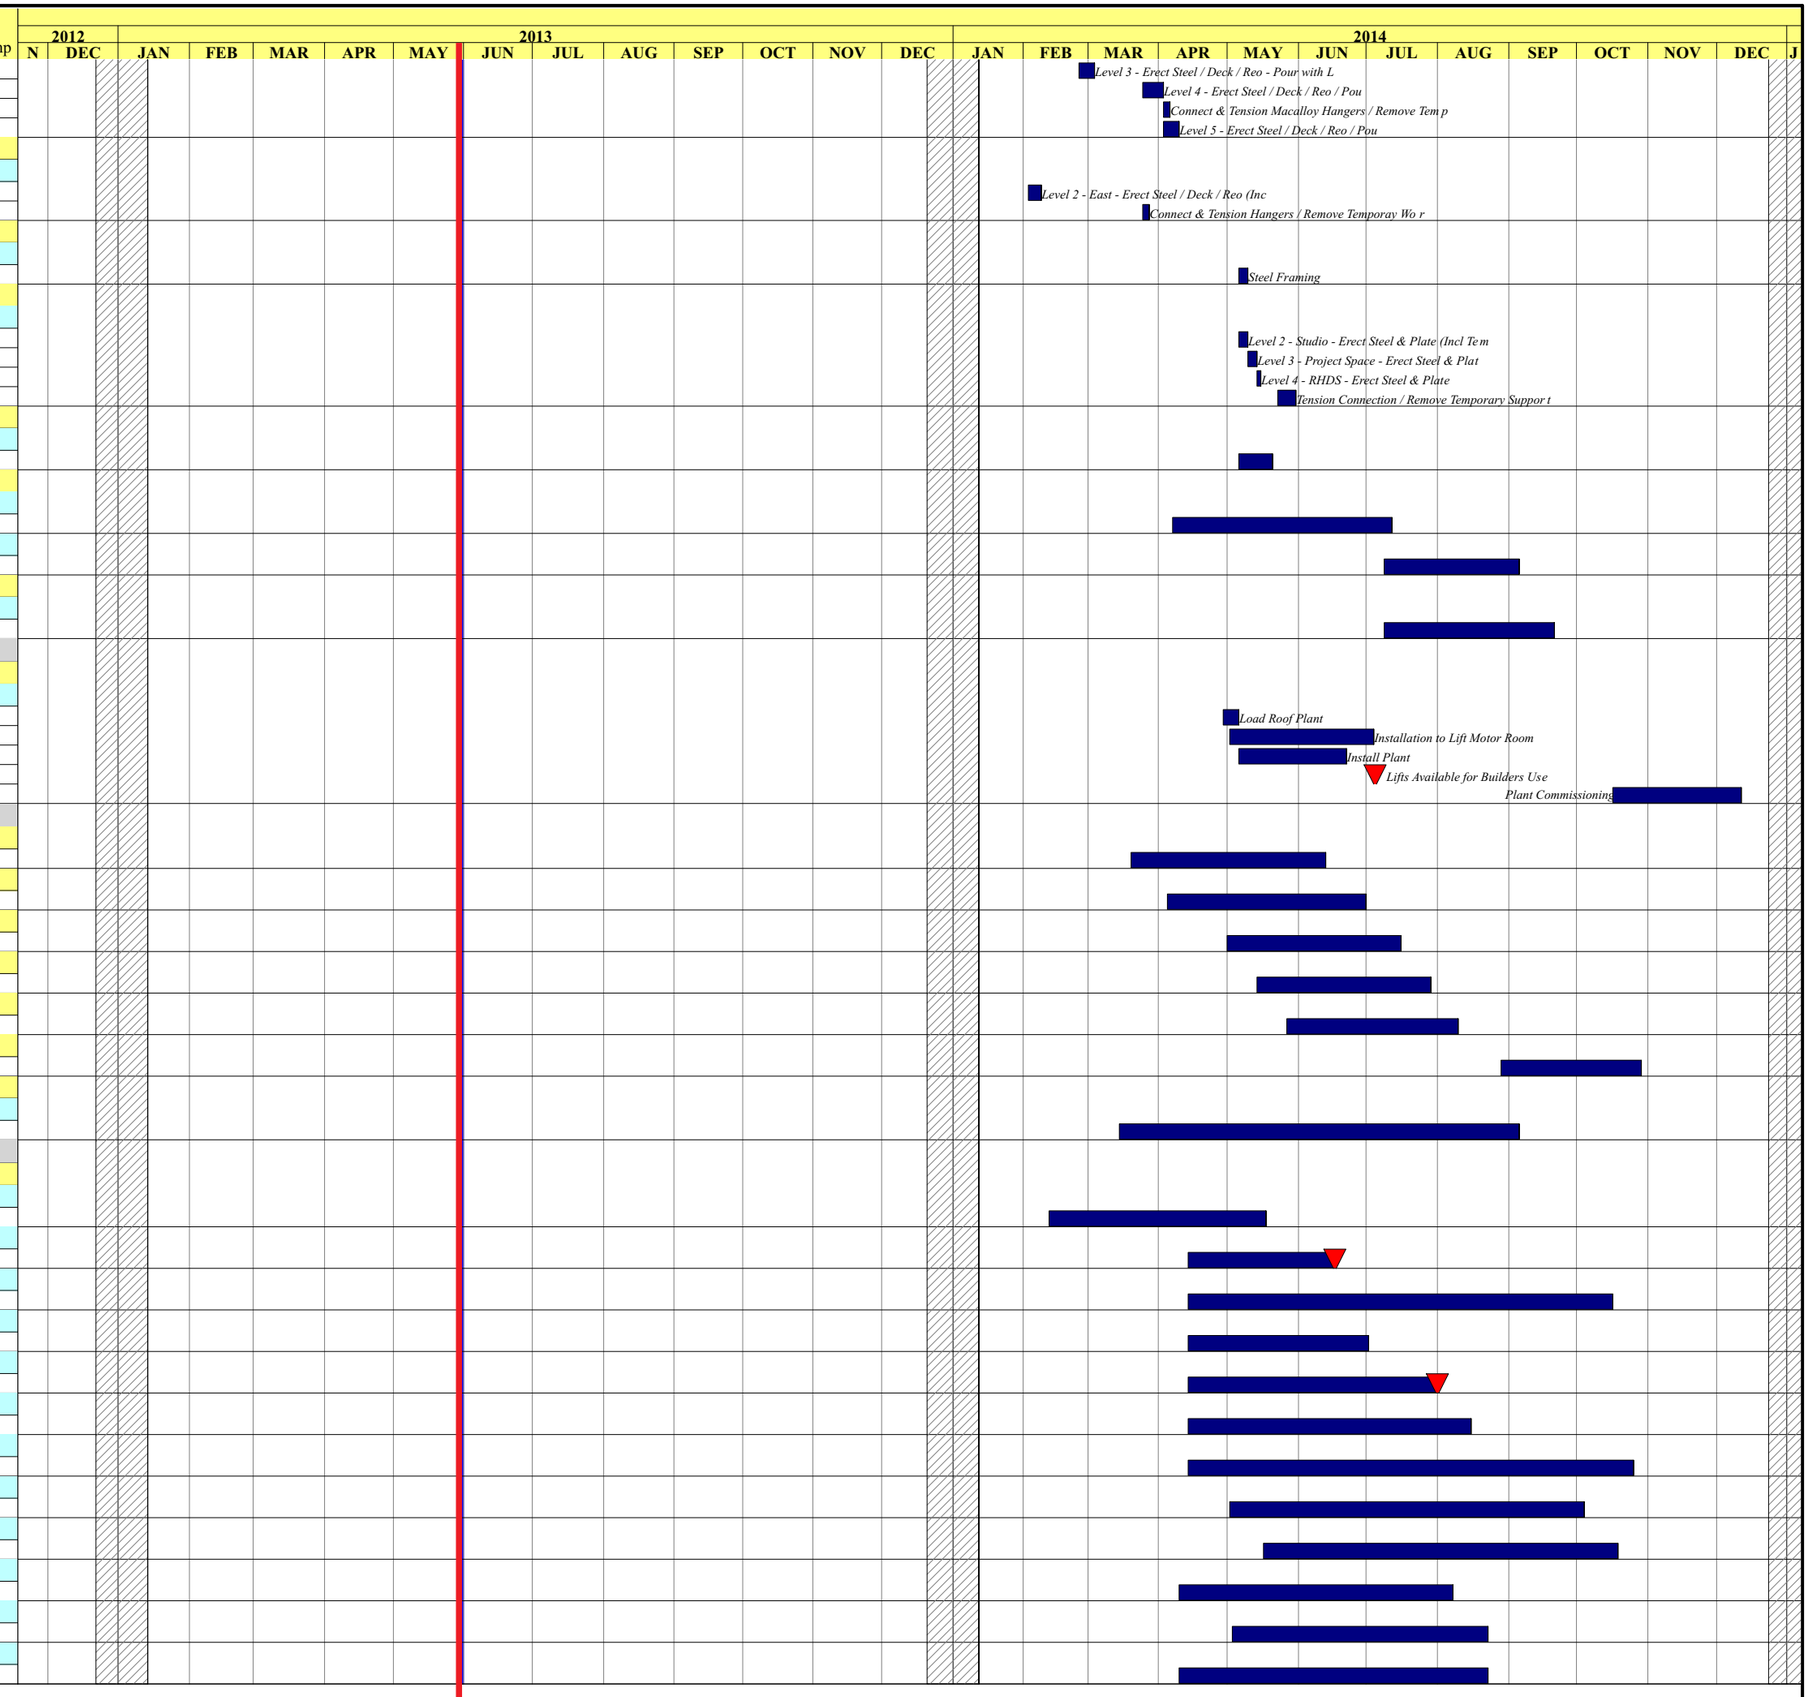

© Primavera Systems, Inc.

Date	Revision	Checked	Approved

Activity ID	Activity description	Dur Days	Early Start	Early Finish	% Comp
+ *LIBRARY - OPEN COMPACTUS*					
		84	27-MAY-14	11-SEP-14	0
+ *AMENITIES*					
		66	05-JUN-14	29-AUG-14	0
+ *BIN STORE / EXHIBITION STORE / BIKE STORE*					
		45	27-JUN-14	22-AUG-14	0
+ *FOYER*					
		114	02-JUN-14	25-OCT-14	0
COMPLETION					
300157310	Services Fit Off Complete	0		22-AUG-14	0
300157360	Power On	1	23-AUG-14	23-AUG-14	0
300157350	Commission	12	25-AUG-14	06-SEP-14	0
300157370	Finishes Complete	0		25-OCT-14	0
300157330	Install Loose Furniture & Fittings	12	27-OCT-14	13-NOV-14	0
300157340	Defects Inspections / Rectification	18	27-OCT-14	21-NOV-14	0
300157320	Final Sign Off	3	22-NOV-14	25-NOV-14	0
300157380	Floor Complete	0		25-NOV-14	0
GROUND FLOOR					
+ *SERVICES ROUGH IN & CORE WALLS*					
		67	15-FEB-14	19-MAY-14	0
+ *PLANT AREAS*					
		36	10-MAY-14	27-JUN-14	0
+ *WORKSHOP*					
		138	16-MAY-14	12-NOV-14	0
+ *LIBRARY*					
		116	05-JUN-14	31-OCT-14	0
+ *EXHIBITION*					
		72	12-JUL-14	10-OCT-14	0
+ *AMENITIES*					
		66	20-MAY-14	13-AUG-14	0
+ *FOYER*					
		122	05-MAY-14	08-OCT-14	0
COMPLETION					
300158910	Services Fit Off Complete	0		20-SEP-14	0
300158960	Power On	1	22-SEP-14	22-SEP-14	0
300158950	Commission	12	23-SEP-14	08-OCT-14	0
300158970	Finishes Complete	0		12-NOV-14	0
300158930	Install Loose Furniture & Fittings	12	13-NOV-14	27-NOV-14	0
300158940	Defects Inspections / Rectification	18	13-NOV-14	05-DEC-14	0
300158920	Final Sign Off	3	09-DEC-14	11-DEC-14	0
300158980	Floor Complete	0		12-DEC-14	0
LEVEL 1					
+ *SERVICES ROUGH IN & CORE WALLS*					
		67	28-FEB-14	31-MAY-14	0
+ *DEAN'S ROOMS*					
		90	21-MAY-14	13-SEP-14	0
+ *NORTHER ROOMS (STUDIO / STUDIO CAD*					
		104	24-MAY-14	06-OCT-14	0
+ *SOUTHERN ROOMS (STUDIO / STUDIO CAD)*					
		98	02-JUN-14	06-OCT-14	0
+ *LARGE SEMINAR ROOMS*					
		82	27-JUN-14	08-OCT-14	0
+ *STUDIO HALL / STUDIO*					
		43	06-SEP-14	30-OCT-14	0
+ *AMENITIES*					
		66	02-JUN-14	26-AUG-14	0
COMPLETION					
300156830	Services Fit Off Complete	0		10-SEP-14	0
300156880	Power On	1	11-SEP-14	11-SEP-14	0
300156870	Commission	12	12-SEP-14	25-SEP-14	0
300156890	Finishes Complete	0		30-OCT-14	0
300156850	Install Loose Furniture & Fittings	12	31-OCT-14	19-NOV-14	0
300156860	Defects Inspections / Rectification	18	31-OCT-14	26-NOV-14	0
300156840	Final Sign Off	3	29-NOV-14	03-DEC-14	0
300156900	Floor Complete	0		03-DEC-14	0
LEVEL 2					
+ *SERVICES ROUGH IN & CORE WALLS*					
		71	15-MAR-14	20-JUN-14	0
+ *IT & FACILITIES WORKSPACE*					
		90	02-JUN-14	24-SEP-14	0
+ *NORTERN STUDIOS*					
		104	05-JUN-14	17-OCT-14	0
+ *WORKSPACE ROOMS*					
		101	21-JUN-14	27-OCT-14	0
+ *SOUTHERN STUDIOS & CAD LAB*					
		104	16-JUN-14	24-OCT-14	0
+ *HANGING STUDIO*					
		66	31-MAY-14	25-AUG-14	0
+ *INFORMAL SPACE ON JUNGLE GYM*					
		26	12-JUL-14	13-AUG-14	0

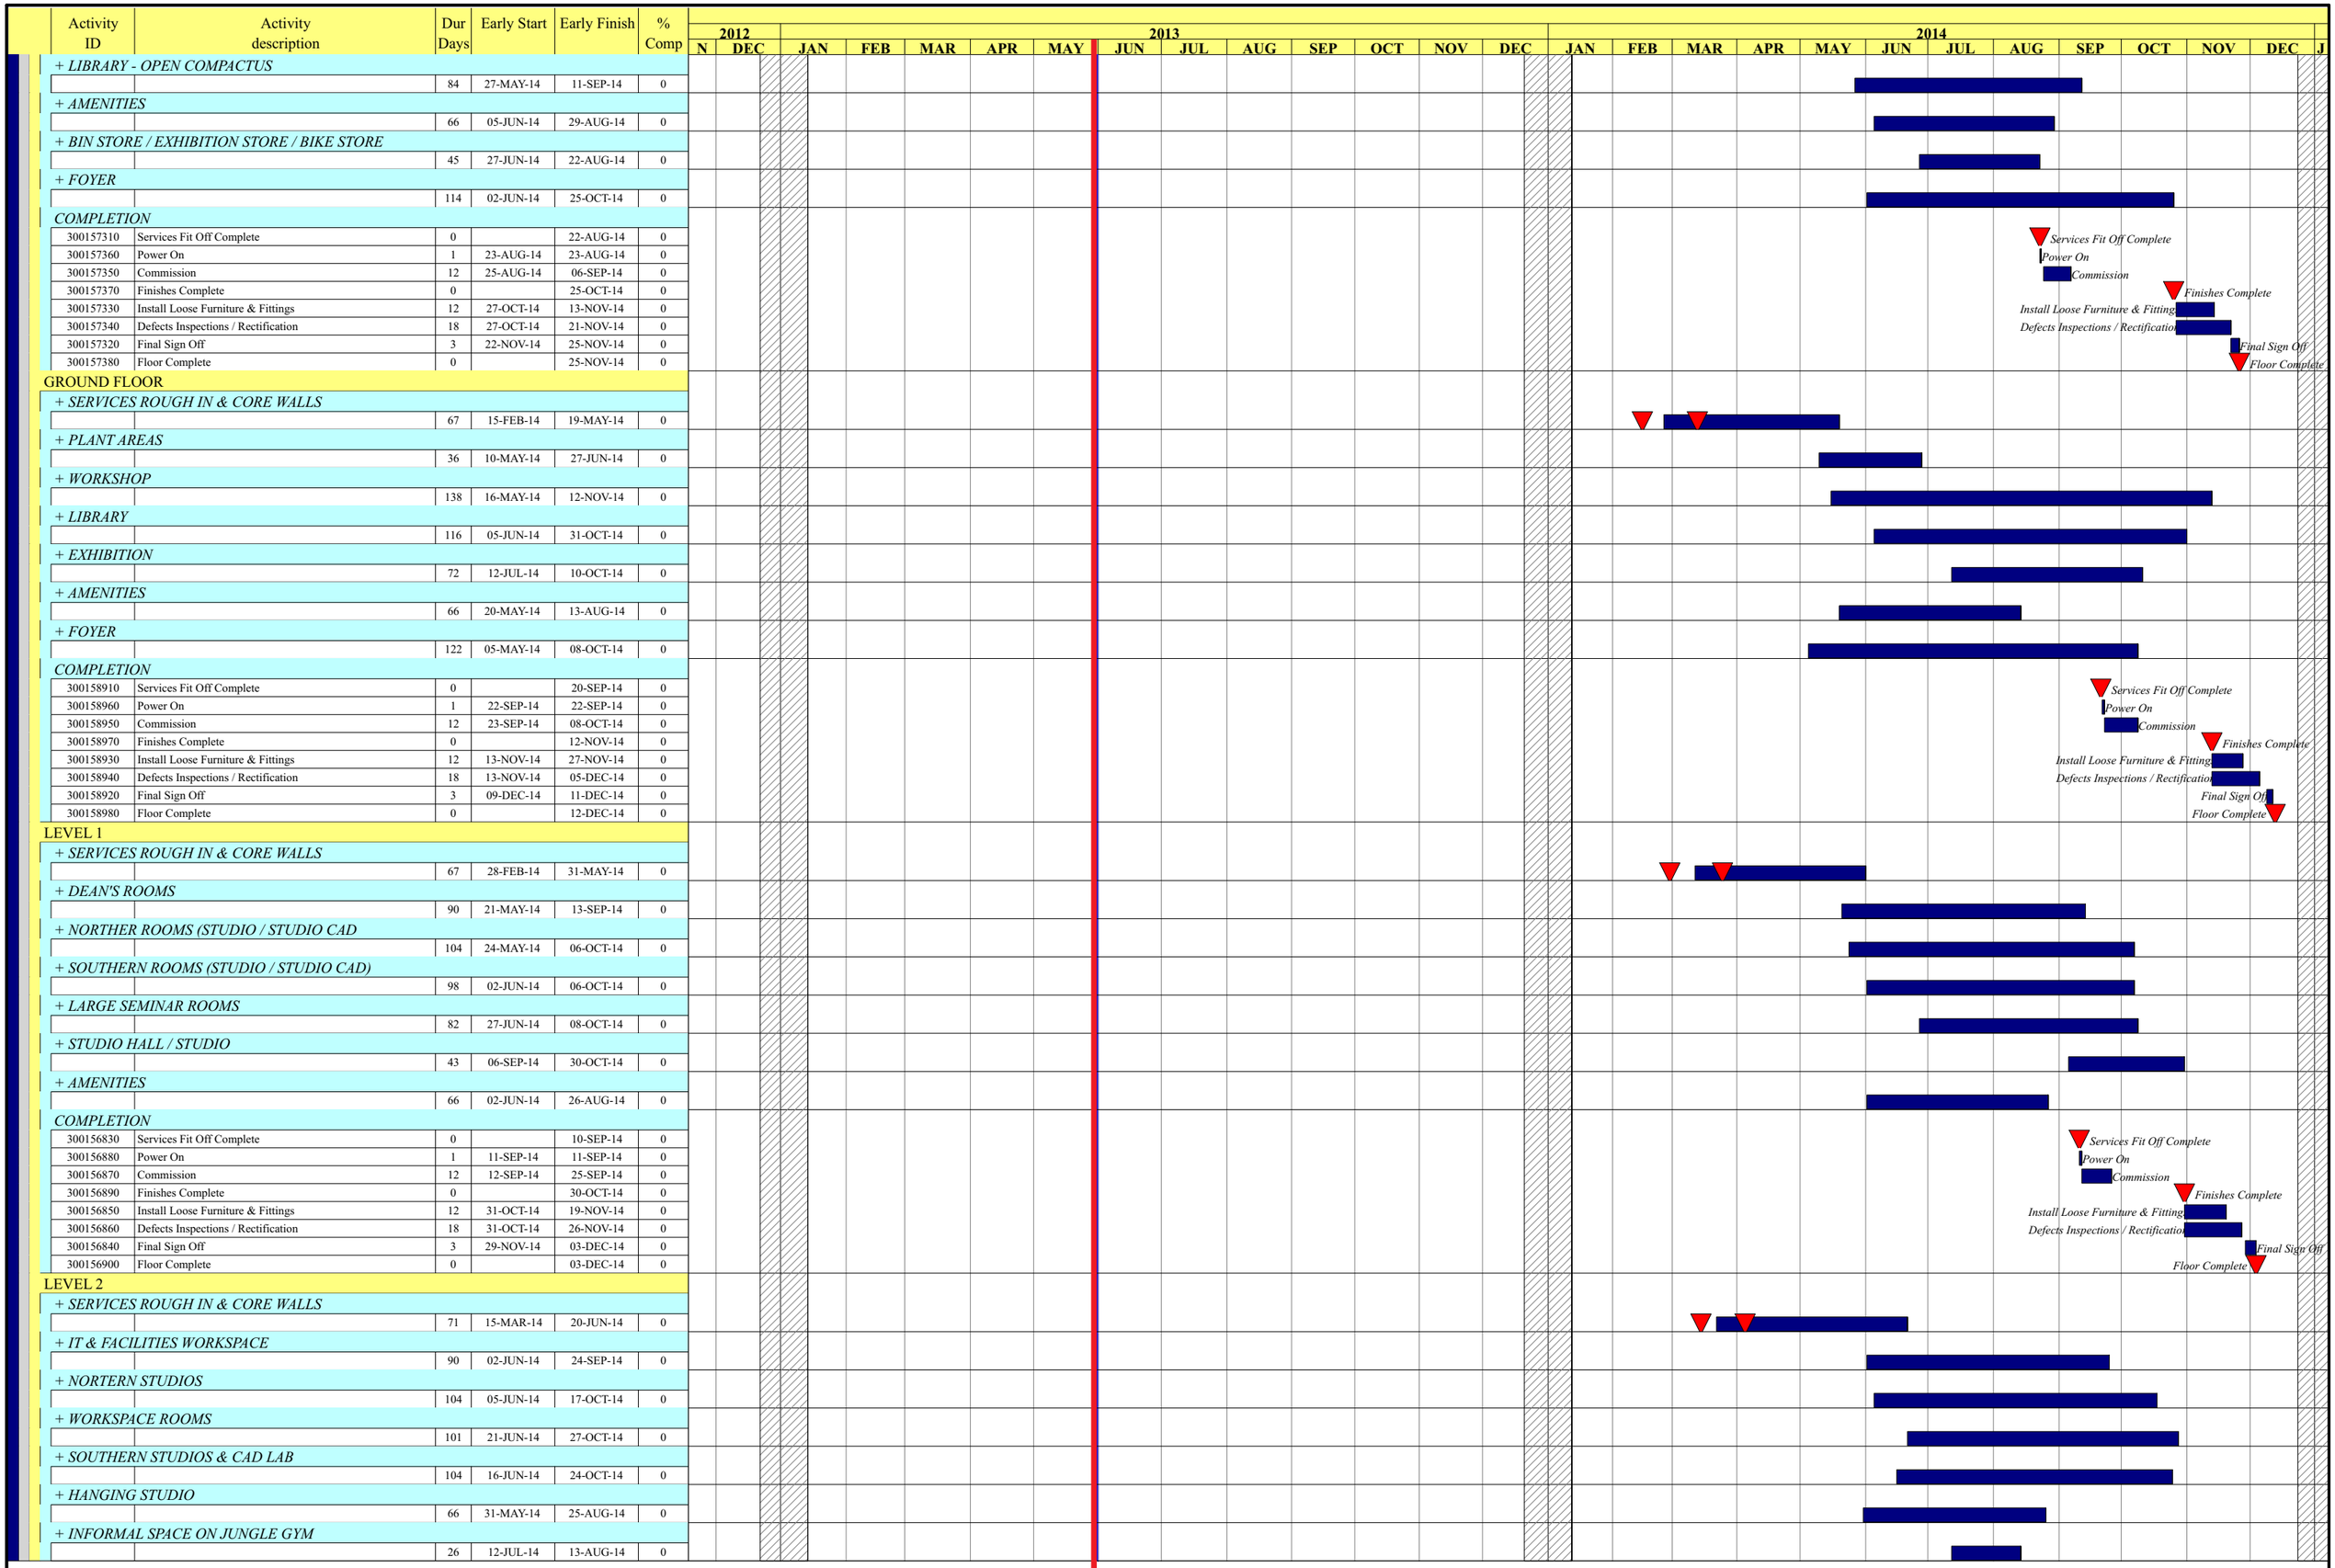

© Primavera Systems, Inc.

Date	Revision	Checked	Approved

Activity ID	Activity description	Dur Days	Early Start	Early Finish	% Comp
+ *AMENITIES*					
		66	16-JUN-14	05-SEP-14	0
COMPLETION					
300154120	Services Fit Off Complete	0		03-OCT-14	0
300154060	Power On	1	04-OCT-14	04-OCT-14	0
300154110	Commission	12	06-OCT-14	20-OCT-14	0
300154050	Finishes Complete	0		27-OCT-14	0
300154070	Defects Inspections / Rectification	18	28-OCT-14	22-NOV-14	0
300154080	Install Loose Furniture & Fittings	12	28-OCT-14	14-NOV-14	0
300154090	Final Sign Off	3	24-NOV-14	26-NOV-14	0
300154100	Floor Complete	0		26-NOV-14	0
LEVEL 3					
+ *SERVICES ROUGH IN & CORE WALLS*					
		60	02-APR-14	26-JUN-14	0
+ *NORTHERN WORKSPACE ROOMS*					
		106	16-JUN-14	27-OCT-14	0
+ *NORTH EASTERN WORKSPACE ROOMS*					
		106	19-JUN-14	30-OCT-14	0
+ *SOUTH EASTERN WORKSPACE ROOMS*					
		102	27-JUN-14	06-NOV-14	0
+ *RHDS WORKSPACE*					
		84	08-JUL-14	21-OCT-14	0
+ *PROF. / RESEARCH / FINANCE / HR / BUSINESS WORKA*					
		84	15-JUL-14	28-OCT-14	0
+ *HANGING PROJECT RESEARCH SPACE*					
		66	16-JUN-14	05-SEP-14	0
+ *AMENITIES*					
		66	27-JUN-14	17-SEP-14	0
COMPLETION					
300154140	Services Fit Off Complete	0		08-OCT-14	0
300154190	Power On	1	09-OCT-14	09-OCT-14	0
300154180	Commission	12	10-OCT-14	24-OCT-14	0
300154200	Finishes Complete	0		06-NOV-14	0
300154160	Install Loose Furniture & Fittings	12	07-NOV-14	21-NOV-14	0
300154170	Defects Inspections / Rectification	18	07-NOV-14	28-NOV-14	0
300154150	Final Sign Off	3	02-DEC-14	04-DEC-14	0
300154210	Floor Complete	0		04-DEC-14	0
LEVEL 4					
+ *SERVICES ROUGH IN & CORE WALLS*					
		60	12-APR-14	08-JUL-14	0
+ *JAPENESE ROOM*					
		98	30-JUN-14	30-OCT-14	0
+ *NORTERN WORK SPACES*					
		106	30-JUN-14	13-NOV-14	0
+ *NORTH EASTERN WORKSPACES*					
		106	01-JUL-14	14-NOV-14	0
+ *SOUTH EASTERN WORKSPACE & ACADEMIC*					
		101	09-JUL-14	15-NOV-14	0
+ *RHDS*					
		84	16-JUL-14	29-OCT-14	0
+ *SOUTHERN STUDIOS*					
		80	24-JUL-14	31-OCT-14	0
+ *STAFF LOUNGE*					
		107	24-JUN-14	08-NOV-14	0
+ *HANGING RHDS*					
		84	24-JUN-14	07-OCT-14	0
+ *AMENITIES*					
		66	09-JUL-14	30-SEP-14	0
COMPLETION					
300154230	Services Fit Off Complete	0		18-OCT-14	0
300154280	Power On	1	20-OCT-14	20-OCT-14	0
300154270	Commission	12	21-OCT-14	07-NOV-14	0
300154290	Finishes Complete	0		15-NOV-14	0
300154250	Install Loose Furniture & Fittings	12	18-NOV-14	02-DEC-14	0
300154260	Defects Inspections / Rectification	17	18-NOV-14	08-DEC-14	0
300154240	Final Sign Off	3	09-DEC-14	11-DEC-14	0
300154300	Floor Complete	0		12-DEC-14	0
EXTERNAL WORKS					
300150520	Roof Terrace (Level 4)	60	11-AUG-14	24-OCT-14	0
300156810	Landscaping	90	11-AUG-14	05-DEC-14	0
300150510	Level 1 Terraces	60	26-AUG-14	12-NOV-14	0
1040	Project Complete	0		12-DEC-14	0

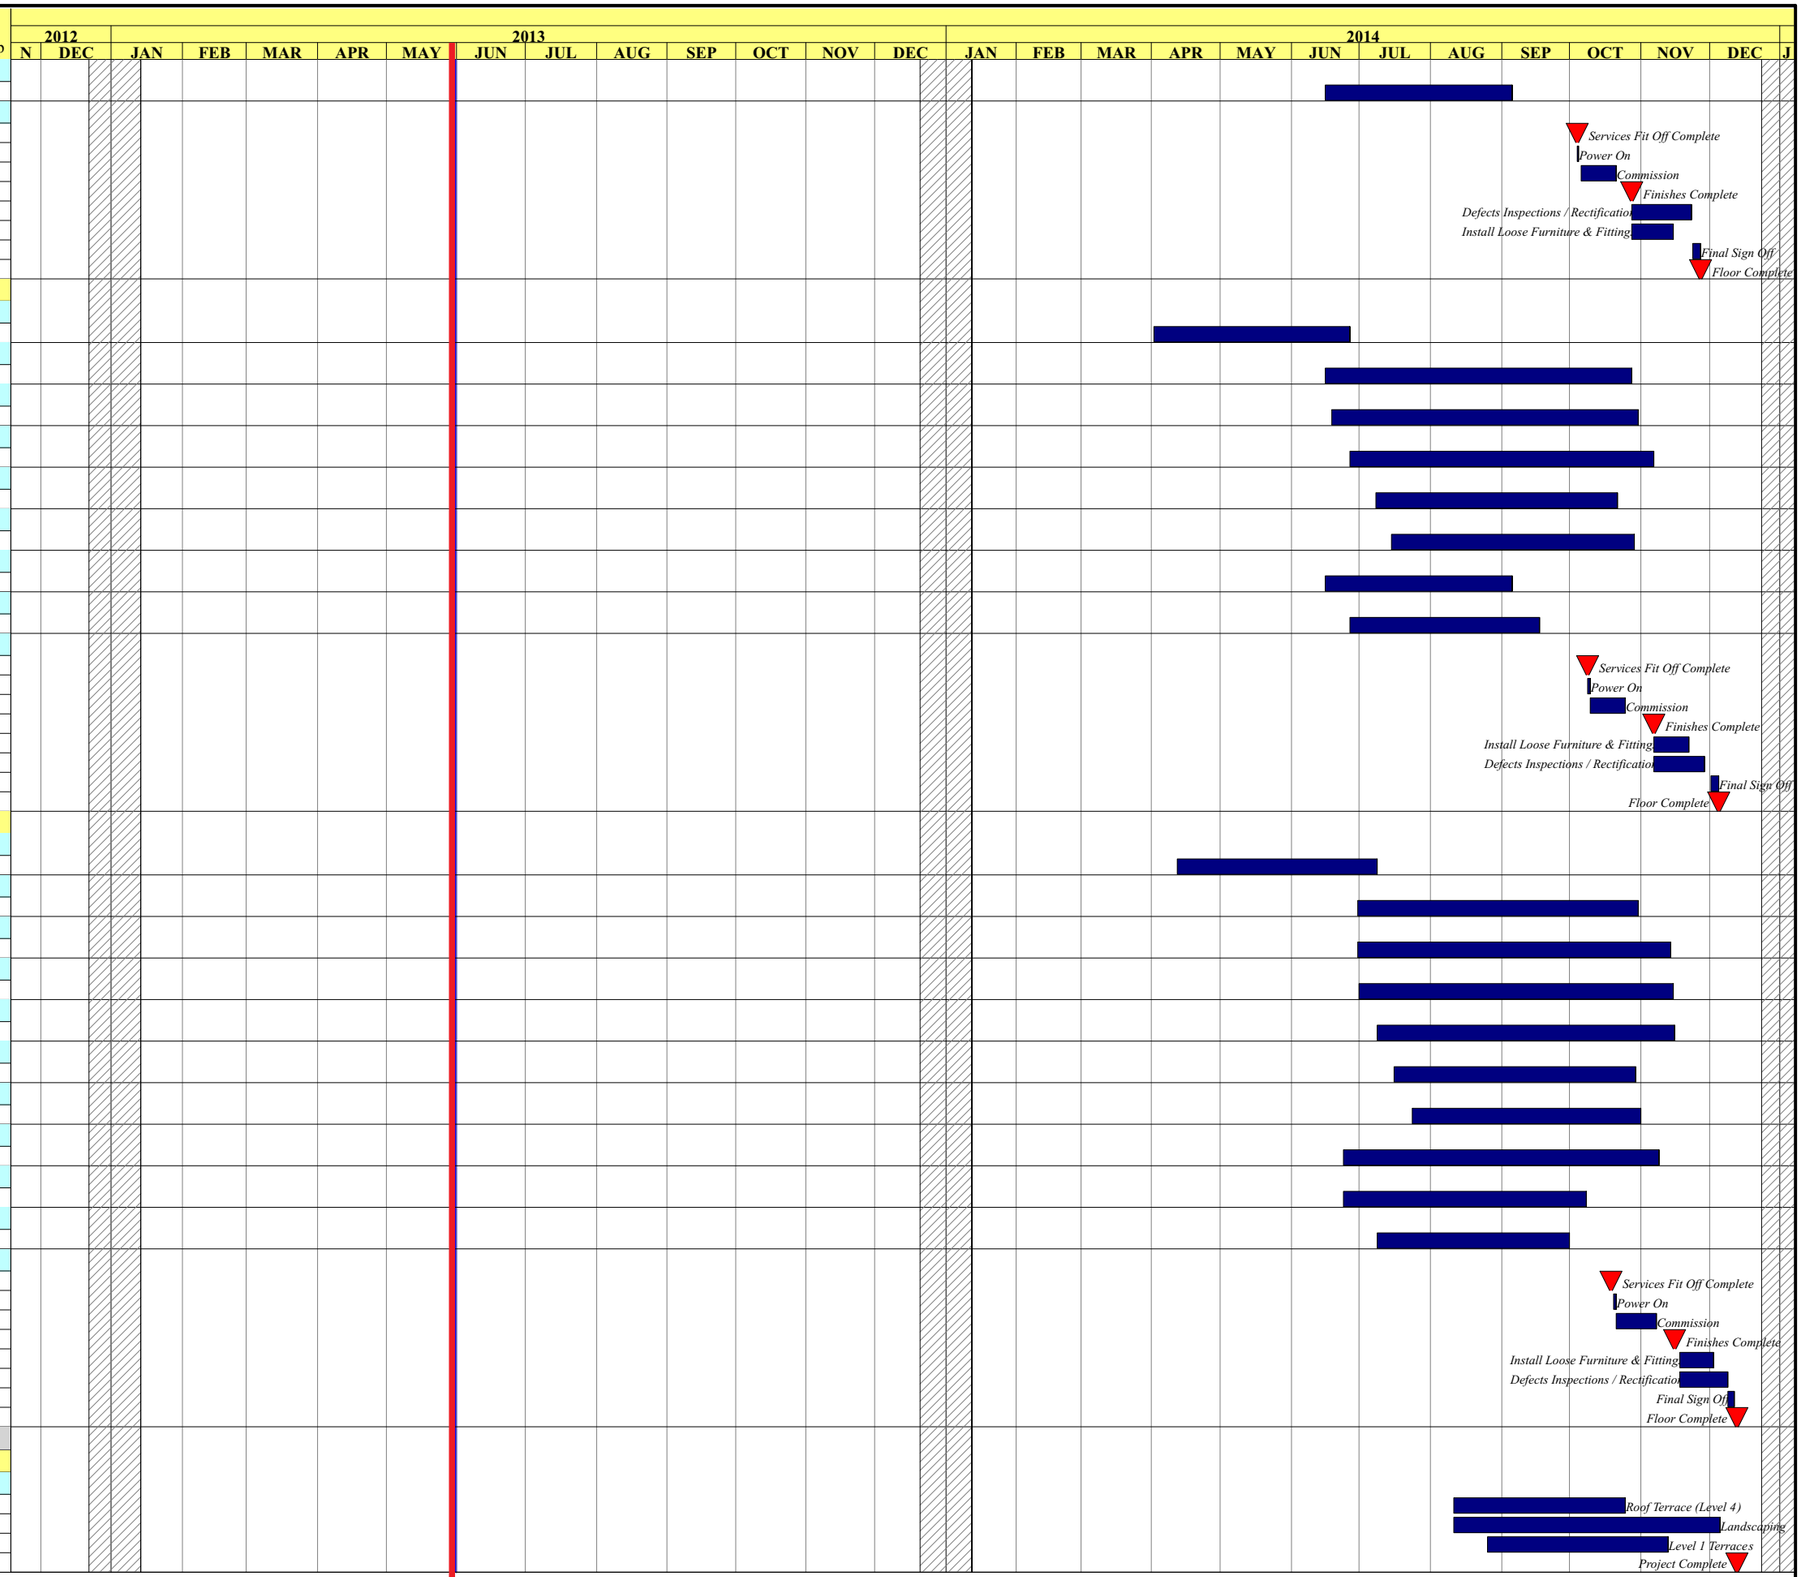

© Primavera Systems, Inc.

Date	Revision	Checked	Approved
