Line	Name	Start	Dur	Finish
1	**Contract**	13 Sep 12	140d	22 Apr 13
2	Head Contractor Appointed	14 Dec 12		14 Dec 12
3	Novation of Design Consultants	17 Dec 12	5d	21 Dec 12
4	Re-document to include for VE	17 Dec 12	65d	28 Mar 13
5	UoM Sign Off VE Items	02 Apr 13	15d	22 Apr 13
6	**Key Milestones**	07 Dec 12	764d	12 Dec 15
7	Contract Award	14 Dec 12		14 Dec 12
8	Enabling & Demolition Works Conclude	02 May 13		02 May 13
9	Main Contractor Site Possession	03 May 13		03 May 13
10	Completion of Basement Retention System Incl Bulk Excavation	29 Aug 13		29 Aug 13
11	Completion of Ground Level Suspended Slabs Incl Library	19 Mar 14		19 Mar 14
12	Completion of Reinforced & Timber Composite Structures to Level 5	28 Apr 14		28 Apr 14
13	Completion of Composite Construction Steel Hanging Structures	30 May 14		30 May 14
14	Completion of Atrium Roof Beam & Glazing Works	08 Jul 14		08 Jul 14
15	Completion of Facade Works (Excluding Hoist Area)	09 Aug 14		09 Aug 14
16	Completion of Facade Works (Including Hoist Area)	12 Sep 14		12 Sep 14
17	Practical Completion	12 Dec 14		12 Dec 14
18	Client Commissioning Complete	20 Feb 15		20 Feb 15
19	Final Completion	12 Dec 15		12 Dec 15
20	**Design & Procurement (Key Packages)**	02 Jan 13	359d	17 Jun 14
21	**Main Construction Works**	07 Dec 12	510d	12 Dec 14
22	**Demolition (By Others)**	07 Dec 12	85d	03 May 13
23	**Site Establishment**	03 May 13	12d	17 May 13
24	**Excavation / Retention / Foundations**	11 May 13	128d	22 Oct 13
25	*Piling*	11 May 13	33d	22 Jun 13
26	*Retention & Excavation*	25 May 13	74d	29 Aug 13
27	*Foundations & Basement Slabs*	10 Aug 13	58d	22 Oct 13
28	**Main Concrete Structure**	19 Oct 13	125d	05 May 14
29	*Ground Level Slab*	19 Oct 13	93d	19 Mar 14
30	*Level 1 Slab*	28 Nov 13	30d	01 Feb 14
31	*Level 2 Slab*	13 Dec 13	25d	11 Feb 14
32	*Level 3 Slab*	01 Feb 14	29d	12 Mar 14
33	*Level 4 Slab*	15 Feb 14	28d	24 Mar 14
34	*Level 5 Slab (Roof)*	28 Feb 14	28d	04 Apr 14
35	**Cantilever Structure**	01 May 14	21d	27 May 14
36	**Roof Works**	05 Apr 14	66d	08 Jul 14
37	*Level 5 Roof Structure*	05 Apr 14	12d	28 Apr 14
38	*Upper Roof Structure*	29 Apr 14	24d	28 May 14
39	*Roof Over Atrium*	21 May 14	36d	08 Jul 14
40	**Atrium Works & Specialised Structures**	13 Dec 13	192d	20 Sep 14
41	*Jungle Gym Structure*	13 Dec 13	70d	09 Apr 14
42	*Link Bridge*	03 Feb 14	41d	27 Mar 14
43	*Studio Mound*	06 May 14	4d	09 May 14
44	*Hanging Studio Steel Frame*	06 May 14	20d	30 May 14
45	*Y-Stair Structure*	06 May 14	12d	20 May 14
46	*Internal Cladding*	07 Apr 14	113d	05 Sep 14
47	Heritage Facade	07 Apr 14	68d	11 Jul 14
48	Hanging Studio & Mound	09 Jul 14	48d	05 Sep 14
49	*Finishes to Atrium*	09 Jul 14	60d	20 Sep 14
50	**Lift & Plant**	29 Apr 14	175d	11 Dec 14
51	**Facade**	15 Mar 14	173d	28 Oct 14
52	*Ground Floor*	20 Mar 14	60d	12 Jun 14
53	*Level 1*	05 Apr 14	60d	30 Jun 14
54	*Level 2*	01 May 14	58d	15 Jul 14
55	*Level 3*	14 May 14	58d	28 Jul 14
56	*Level 4*	27 May 14	58d	09 Aug 14
57	*Hoist Location*	29 Aug 14	48d	28 Oct 14
58	*Joseph Reed Facade Works*	15 Mar 14	132d	05 Sep 14
59	**Services & Finishes**	12 Feb 14	228d	12 Dec 14
60	*Basement*	12 Feb 14	215d	26 Nov 14
61	*Ground Floor*	15 Feb 14	225d	12 Dec 14
62	*Level 1*	28 Feb 14	208d	04 Dec 14
63	*Level 2*	15 Mar 14	193d	27 Nov 14
64	*Level 3*	02 Apr 14	184d	05 Dec 14
65	*Level 4*	12 Apr 14	181d	12 Dec 14
66	**External Works**	11 Aug 14	90d	05 Dec 14
67	Project Complete	12 Dec 14		12 Dec 14

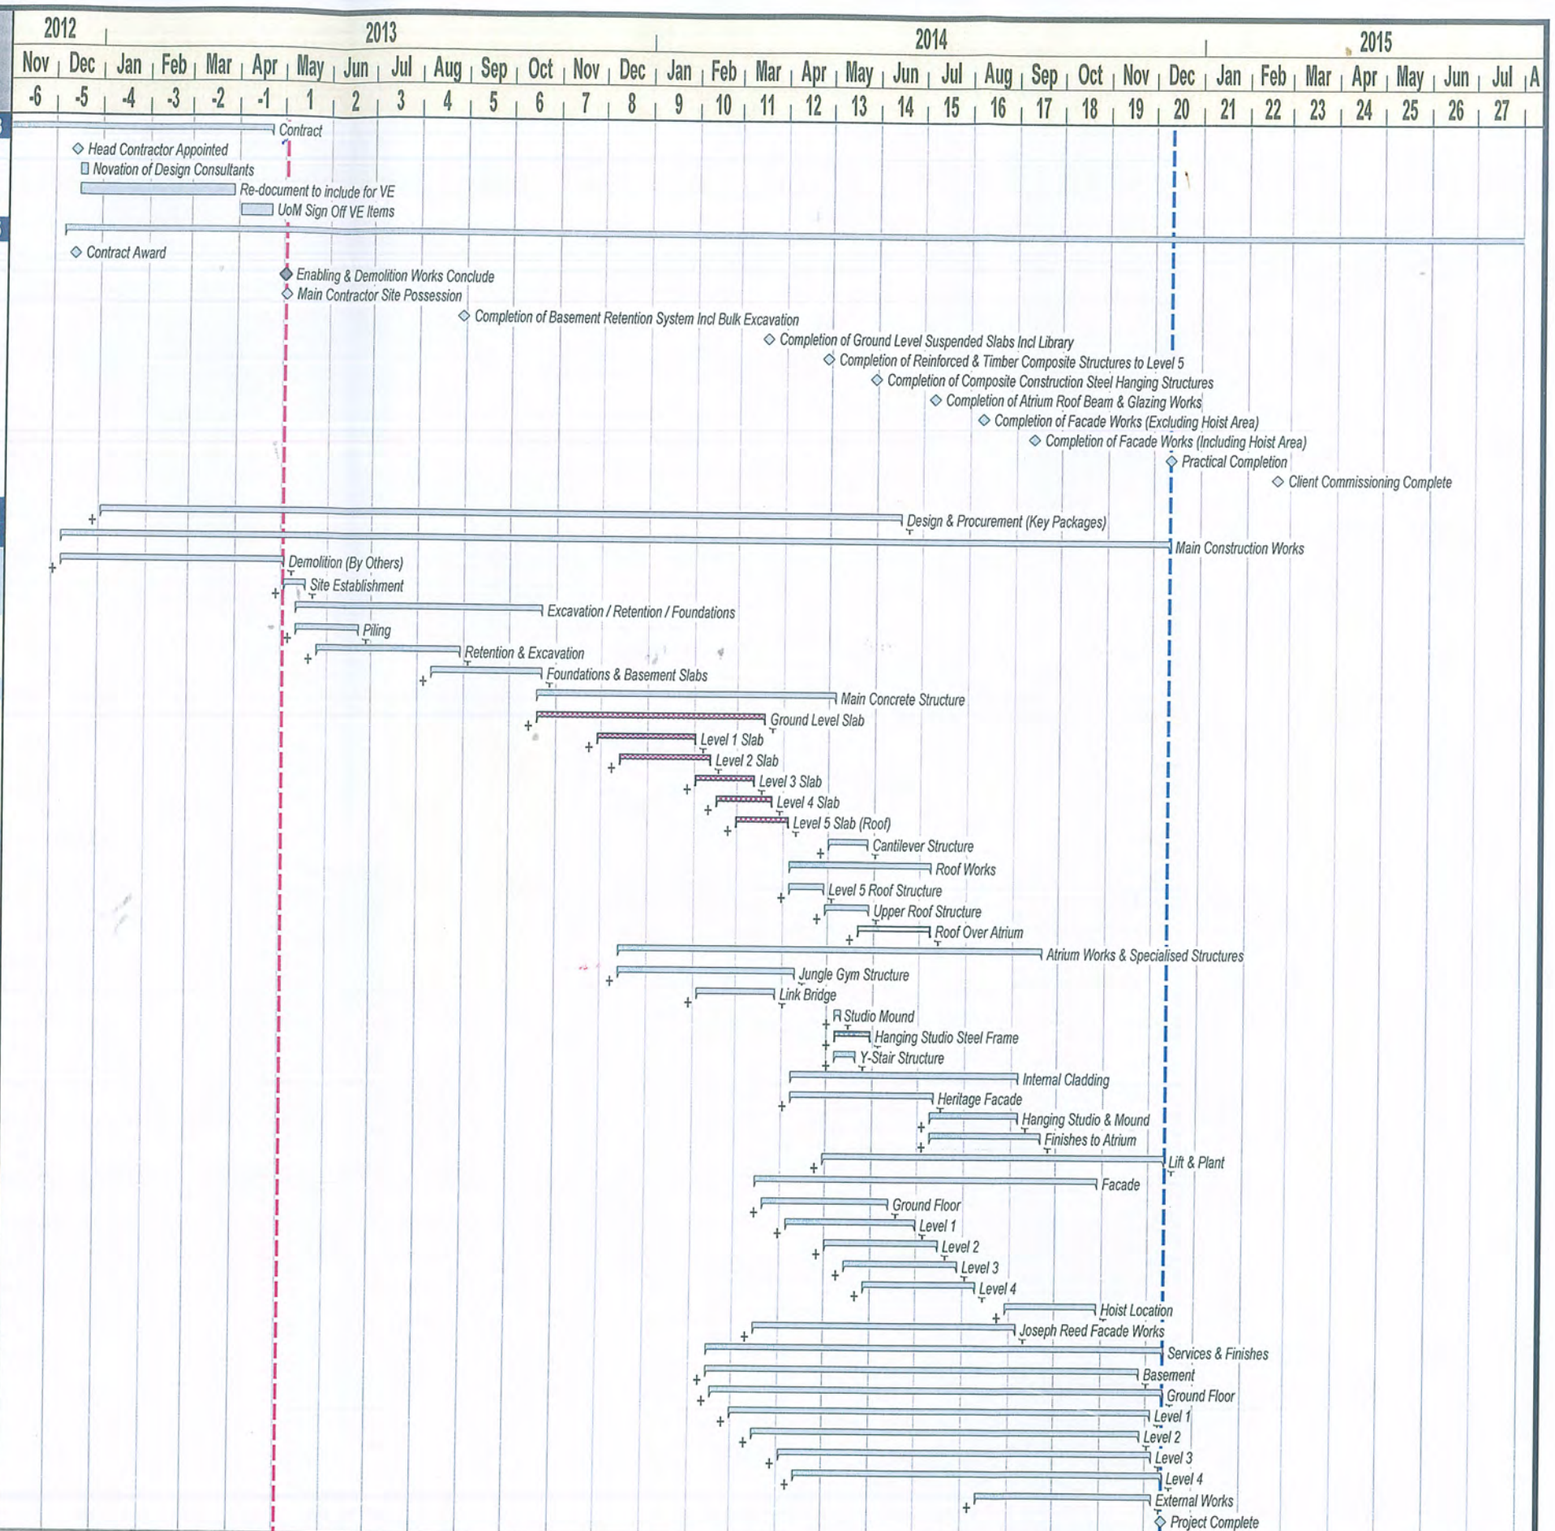

Brookfield MULTIPLEX | BM 50 YEARS

University of Melbourne - FABP

Contract Programme - Revision 10 - Summary

Project Ref. C:\Documents and Settings\peterg\My Documents\Projects\Melbourne\Uni Of Melb FABP\Melb Uni FABP - Rev 10 - Contract Programme.pp

Revision Date 21/11/2012
Revision Number 10
Print Date 19/03/2013
Programme Number BMC - FABP - 10 - C - 1000

18.03.13
